




HANNEY & ASSOCIATES, ARCHITECTS
1726 South Hillside, Wichita, Kansas, 67211
Phone (316) 883-8965
Fax (316) 884-1441
www.hanarchitects.com

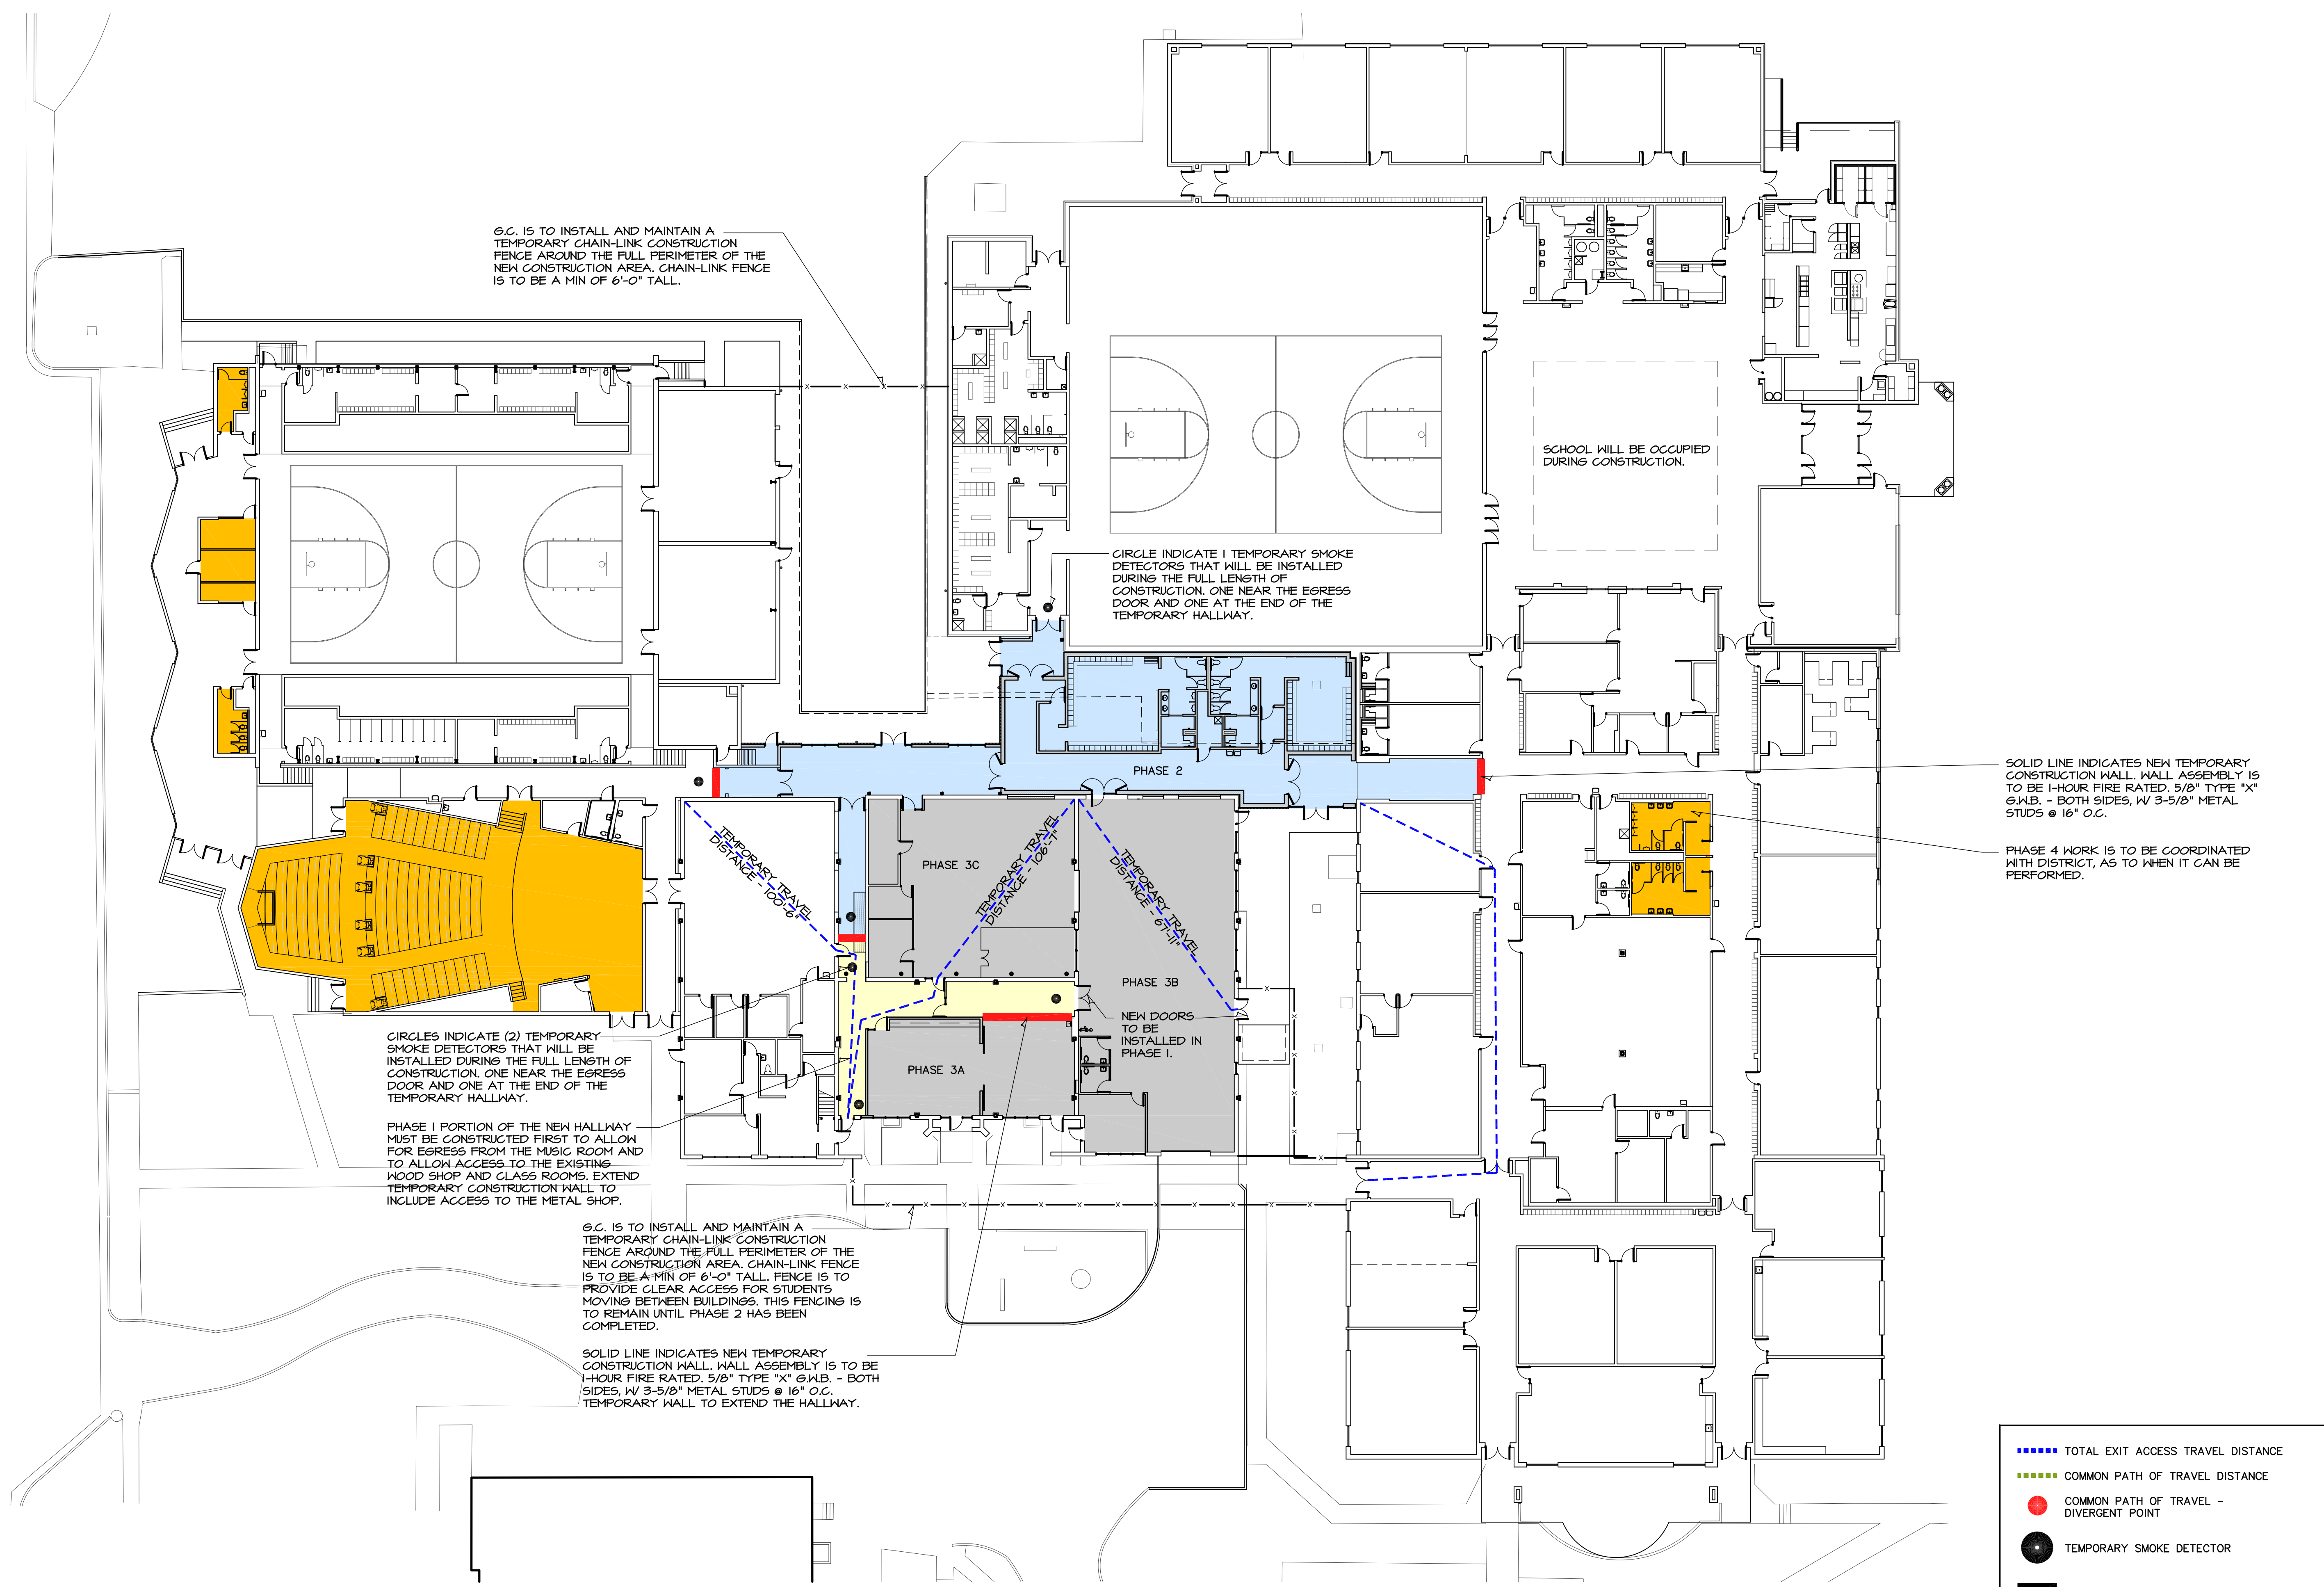

2019
OXFORD JUNIOR/SENIOR HIGH SCHOOL
UNIFIED SCHOOL DISTRICT #358
 515 N Water St, Oxford, KS 67119

G.C. IS TO INSTALL AND MAINTAIN A TEMPORARY CHAIN-LINK CONSTRUCTION FENCE AROUND THE FULL PERIMETER OF THE NEW CONSTRUCTION AREA. CHAIN-LINK FENCE IS TO BE A MIN OF 6'-0" TALL.

SCHOOL WILL BE OCCUPIED DURING CONSTRUCTION.

CIRCLE INDICATE (1) TEMPORARY SMOKE DETECTORS THAT WILL BE INSTALLED DURING THE FULL LENGTH OF CONSTRUCTION. ONE NEAR THE EGRESS DOOR AND ONE AT THE END OF THE TEMPORARY HALLWAY.

SOLID LINE INDICATES NEW TEMPORARY CONSTRUCTION WALL. WALL ASSEMBLY IS TO BE 1-HOUR FIRE RATED, 5/8" TYPE "X" G.W.B. - BOTH SIDES, W/ 3-5/8" METAL STUDS @ 16" O.C.

PHASE 4 WORK IS TO BE COORDINATED WITH DISTRICT, AS TO WHEN IT CAN BE PERFORMED.

CIRCLES INDICATE (2) TEMPORARY SMOKE DETECTORS THAT WILL BE INSTALLED DURING THE FULL LENGTH OF CONSTRUCTION. ONE NEAR THE EGRESS DOOR AND ONE AT THE END OF THE TEMPORARY HALLWAY.



PHASE 1 PORTION OF THE NEW HALLWAY MUST BE CONSTRUCTED FIRST TO ALLOW FOR EGRESS FROM THE MUSIC ROOM AND TO ALLOW ACCESS TO THE EXISTING WOOD SHOP AND CLASS ROOMS. EXTEND TEMPORARY CONSTRUCTION WALL TO INCLUDE ACCESS TO THE METAL SHOP.

G.C. IS TO INSTALL AND MAINTAIN A TEMPORARY CHAIN-LINK CONSTRUCTION FENCE AROUND THE FULL PERIMETER OF THE NEW CONSTRUCTION AREA. CHAIN-LINK FENCE IS TO BE A MIN OF 6'-0" TALL. FENCE IS TO PROVIDE CLEAR ACCESS FOR STUDENTS MOVING BETWEEN BUILDINGS. THIS FENCING IS TO REMAIN UNTIL PHASE 2 HAS BEEN COMPLETED.

SOLID LINE INDICATES NEW TEMPORARY CONSTRUCTION WALL. WALL ASSEMBLY IS TO BE 1-HOUR FIRE RATED, 5/8" TYPE "X" G.W.B. - BOTH SIDES, W/ 3-5/8" METAL STUDS @ 16" O.C. TEMPORARY WALL TO EXTEND THE HALLWAY.

A TEMPORARY EGRESS & WALLS

SCALE: 1" = 20'-0"



- TOTAL EXIT ACCESS TRAVEL DISTANCE
- COMMON PATH OF TRAVEL DISTANCE
- COMMON PATH OF TRAVEL - DIVERGENT POINT
- TEMPORARY SMOKE DETECTOR
- TEMPORARY WALL
- PHASE 1 - EGRESS
- PHASE 2 - NEW CONSTRUCTION
- PHASE 3 - CLASSROOM REMODEL
- PHASE 4 - AUDITORIUM & RESTROOM REMODEL

DRAWINGS ISSUED		
NO.	DATE	ITEM ISSUED
① 1/21/20 ADDENDUM # 3		

COMPUTER DRAWING

DATE: AUGUST, 2019
DRAWN BY: MH, CH, MB, JC CHECKED BY: MRH

SHEET

CODE 3

OF 1 SHEETS
